

Construction update




1. Summary
2. Program
3. Appointed contractor
4. Images updates
5. Health & Safety



Summary update



- This update cover work carried out up until the end of August 2017
- The third and fourth floor have now been built up and the concrete floors have been poured.
- The final two floors on the block are under construction.
- The blockwork and SFS has started to be installed the M&E contractor is due to start on site before the end of September .
- The internal walls have been set out and are under construction
- Joinery package is being awarded within the next two weeks for contractor to start 2nd week October
- The steel has now been fire treated now
- Building control have been on site on a regular basis and have been signing off all work as compliant to building regulations.

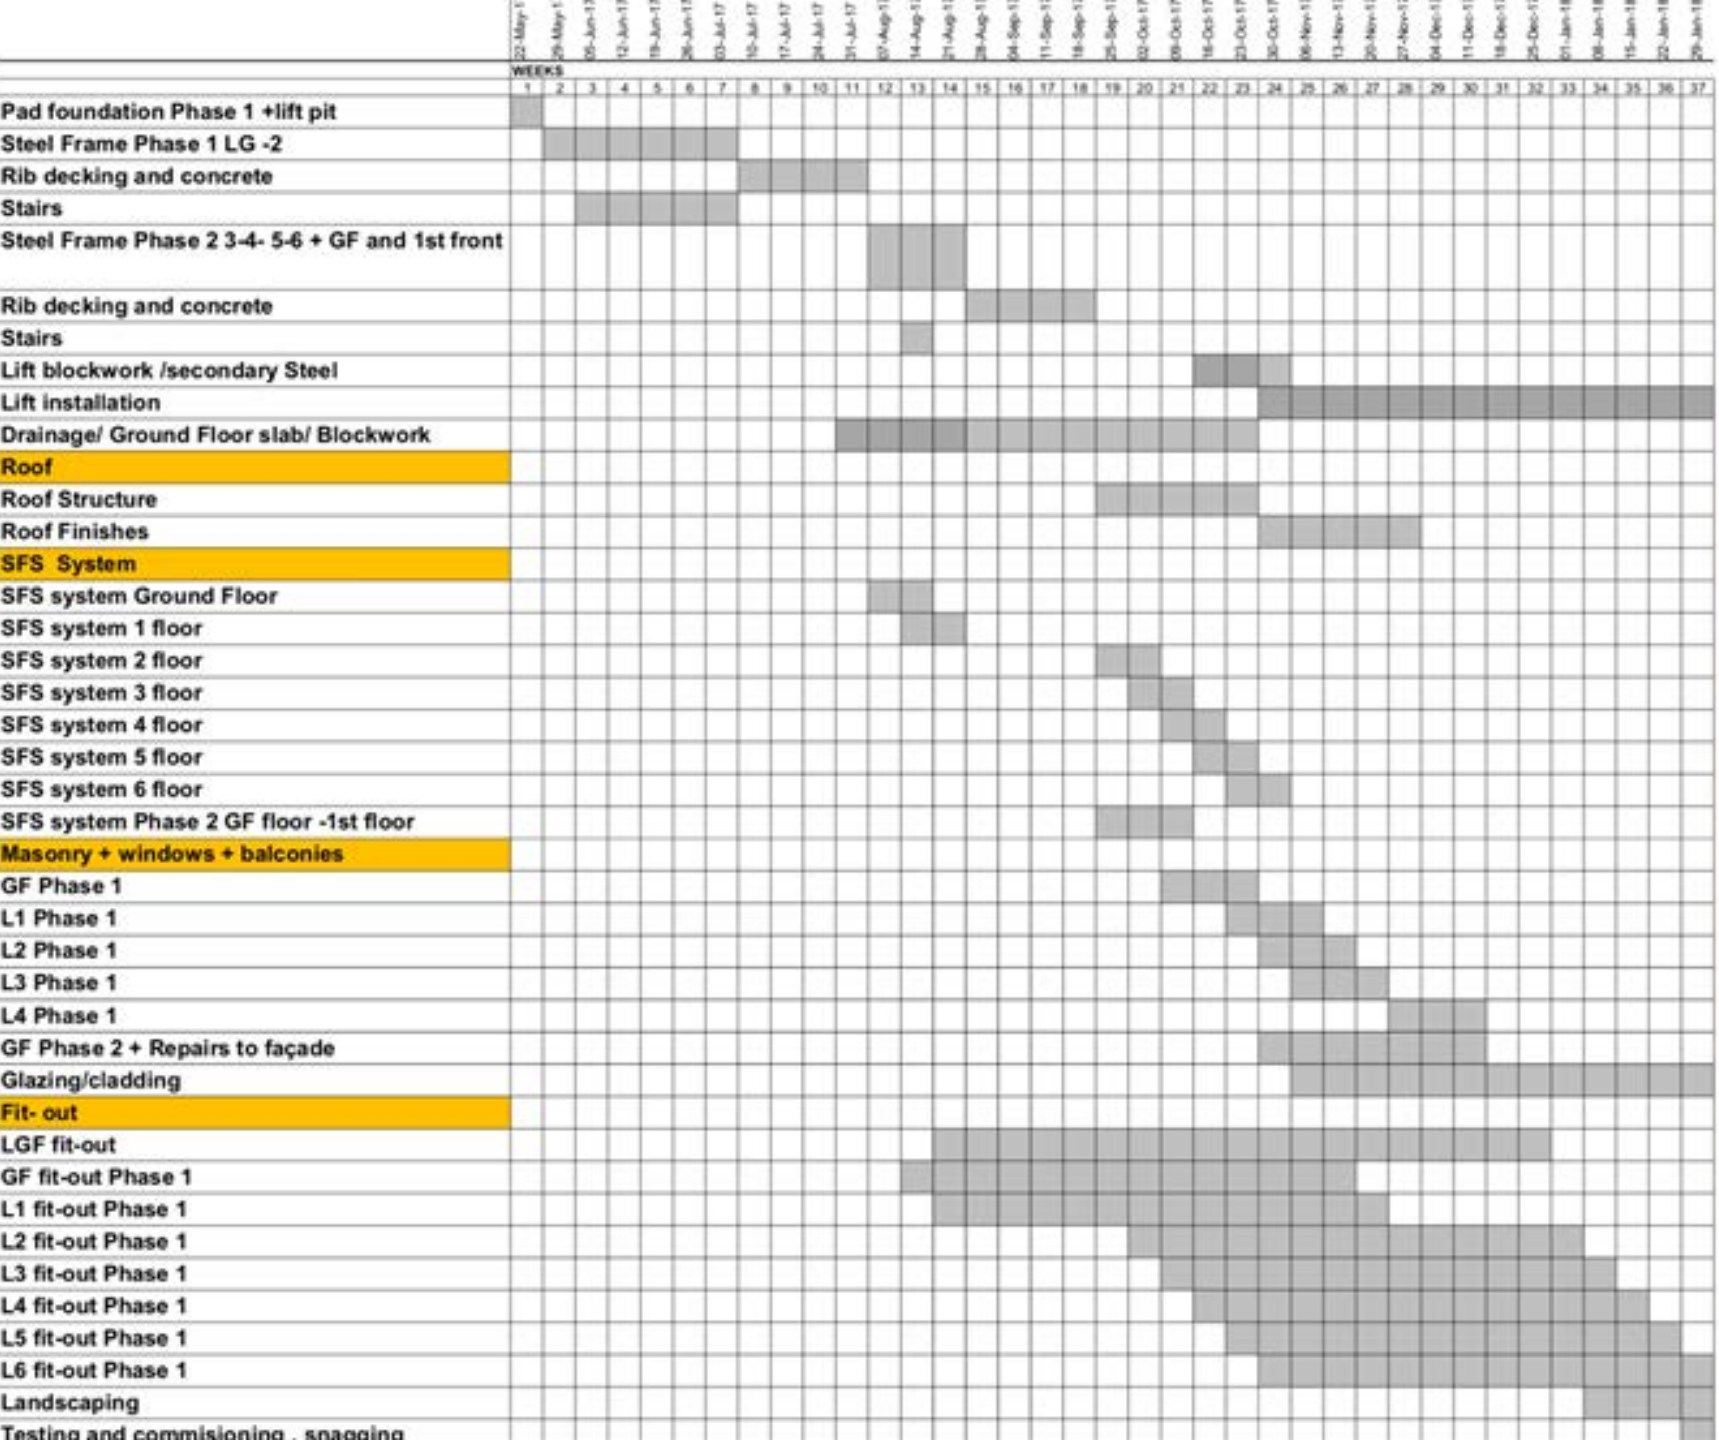



Health & Safety

- Site Manager has reported no accidents on site.
- Rawlings the appointed CDMC have reported site to be safe working place

